

1 Regarding: 3705 Bartlett Dr Cookeville TN 38506-7414
PROPERTY ADDRESS

Version 01/01/2026



TENNESSEE DEPARTMENT OF ENVIRONMENT AND CONSERVATION APPLICATION FOR GROUND WATER PROTECTION SERVICES

Daf

1. SERVICE REQUESTED: (check service)	APPLICANT COMPLETE QUESTIONS:	FEES DUE	PTBMIS CODES V689 Code Supp/Code
☒ Septic System Construction Permit			
Dwelling	2, 3, 4, 7, 8, 9	\$	78064 Yes
Commercial: gpd	2, 3, 4, 7, 8, 9	\$	78064 Yes
☒ System Modification	2, 3, 4, 7, 8, 9	\$ 200.00	78064 Yes
Repair	2, 3, 4, 7, 8, 9	\$	78032
Inspection Letter	2, 3, 5, 7, 8, 9	\$	78030
Water Sample			
Total Coliform	2, 3, 6, 7, 8, 9	\$	78036 Yes
Fecal Coliform	2, 3, 6, 7, 8, 9	\$	78038 Yes
Alternative System Permit*		\$	78068
Large Conventional System Plan Review*		\$	78090
Large Alternative System Plan Review*		\$	78090
Experimental System Plan Review*		\$	78072
Subdivision Evaluation: Lots		\$	78084
Soil Mapping: Type Acres		\$	Yes
Installer Permit: Type(s)		\$	78026 Yes
Pumper Permit*		\$	78028
Plat Approval — Individual Lot		\$	78029
Domestic Septage Disposal Site Permit		\$	78031

*Applicant may review these service requests with Environmental Specialist prior to processing application.

2. **LANDOWNER:** Names: Steve Baugh Address: 3705 Bartlett Dr Cookeville TN 38501 Day Phone: 520-1708

3. **APPLICANT** Name: _____ Address: _____ Day Phone: _____

4. **ORIGINAL OWNER** Name: _____

5. **LOCATION OF LOT OR SITE:** a) In a subdivision? ☒ b) Name: First Lake Lot # 55

6. **FOR SSDS PERMIT ONLY:** a) Size of lot: 120x100x143 b) Number of Bedrooms: 1

c) How many occupants? 2 d) Excavated Basement? Yes ☐ No ☒

e) Basement Plumbing Fixtures? Yes ☐ No ☒

f) Amount of water used monthly (gallons) _____

g) Water Supply: Public ☒ Well ☐ Spring ☐

h) Is the lot staked? ☐ If not, date it will be staked: _____

i) Is the house staked? ☒ If not, date it will be staked: _____

j) Installer, if known: AAA Backhoe

7. **FOR INSPECTION LETTER ONLY:** Will pick up _____ Please mail _____

a) Age of house _____ b) Is house vacant? _____ How long? _____

c) Original sewage system inspected _____

d) Date of previous repairs _____ Inspected _____

e) Is waste water "backing up" into plumbing fixtures? _____ Surfacing on the ground? _____

f) All waste water including washing machines routed into septic tank _____

8. **FOR WATER SAMPLE ONLY:** a) Source of Supply: Spring _____ Well _____

b) Is there an outside faucet? _____ c) Is the source chlorinated? _____

d) For Wells: Is the casing 6" above the ground? _____ Is a sanitary seal on the casing? _____

9. **MAKE A ROUGH SKETCH ON BACK OF THIS WHITE PAGE SHOWING DIRECTIONS TO PROPERTY, PROPERTY LINES, HOUSE SITE, WELL LOCATION, SPRING LOCATION, PLANNED DRIVEWAY AND UTILITIES.**

10. **ALL FEES DUE IN ADVANCE AND ARE NON-REFUNDABLE (except upon appeal). See Fee Schedule on reverse. Make check payable to: TREASURER, STATE OF TENNESSEE**

11. **I certify that the above information is true and correct to the best of my knowledge, and that I have been authorized by the above named landowner to submit this Application for Environmental Services to the Division of Ground Water Protection.**

DATE: 4/22/03 SIGNATURE: [Signature] AMOUNT PAID: \$ 200.00 RECEIPT NUMBER: 07C-1957

White: File

Canary: Owner

**TENNESSEE DEPARTMENT OF ENVIRONMENT AND CONSERVATION
DIVISION OF GROUND WATER PROTECTION
PERMIT FOR CONSTRUCTION OF SUBSURFACE SEWAGE DISPOSAL SYSTEM**

Issued to: <u>Steve Baugh</u> Owner, Developer, Contractor, Installer, Etc. Location: <u>3705 Bartlett Dr.</u> Installation: ☒ 1. New Installation ☐ 2. Repair to Existing System Establishment: ☒ 1. Residential: # Bedrooms <u>1</u> ☐ 2. Other: _____ (specify) Gal/Day: _____	Evaluation Based Upon: ☐ 1. Soil typing by Soil Scientist ☐ a. General ☐ b. High Intensity ☐ c. Extra High Intensity ☒ 2. Soil Percolation Test ☒ 3. Environmental Specialist Estimated Absorption Rate: <u>45</u> MPI Approval based upon: Statute No. <u>T.C.A. 68-221-403</u> ☐ (c) Percolation test ☐ (d) Grandfather clause. Current standards except those specified ☐ (f) 12" (karst) and 6" (non-karst) buffer required ☐ (i) 9" buffer required (24"-36" total soil depth) ☐ (k) Grandfather clause — meets June 30, 1990 standards (repair only) ☐ Other: <u>Reg's</u>	Type of System: ☒ 1. Conventional ☐ 2. Low Pressure Pipe ☐ 3. Mound ☐ 4. Lagoon ☒ 5. Large Diameter Gravelless Pipe ☐ a. Sand backfill required ☐ 6. Other
---	---	--

This system shall consist of a two compartment septic tank holding Existing gallons, with 100 linear feet in 1 trenches, 36 inches wide and 24-30 inches deep. (Depth of gravel: 12 inches)

Also required:
☐ 1. Soil Improvement Practice (SIP)
☐ 2. Flow Diversion Valve
☐ 3. Sewage Pump
☐ 4. Other: _____

All installers of subsurface sewage disposal systems must hold a valid annual license from the Tennessee Department of Environment and Conservation.

The recipient of this permit agrees to construct or have constructed the above described system in accordance with T.C.A. 68-221-401 et. seq. and The Regulations To Govern Subsurface Sewage Disposal Systems. If any part of the system is covered before being inspected and approved, it shall be uncovered by the recipient of the permit at the direction of personnel of the Department of Environment and Conservation. **Any cutting, filling or alterations of the soil conditions on the aforementioned property after this day may render this approval null and void.**

Issued at: <u>Cookeville</u> By: <u>Daniel Phillips, G.S.</u> (Name and Title)	Date: <u>6-11-3</u> Tennessee, in <u>Putnam</u> County Date: <u>30 April '03</u> (Date of Issue)
---	--

This permit is valid for 3 years from date of issue.

Notes 	JD 08/31/26 RD 08/31/26 RD
---------------	--

This is a permit to construct and is not intended to imply approval of any work proposed or completed on this lot.



23 **PERMIT FOR CONSTRUCTION OF SUBSURFACE SEWAGE DISPOSAL SYSTEM**


42505

Issued to: <u>Donald Murphy</u> Owner, Developer, Contractor, Installer, Etc. To be constructed by: <u>Bob Vuck</u> (Installer) Construction of a subsurface sewage disposal system is hereby authorized at: <u>Lot 55, Lakeside S/D</u> (No. and street; Subdivision name and lot no.) Such a system shall consist of a septic tank of <u>400</u> gals. with <u>300</u> linear feet in <u> </u> trenches, <u>36</u> inches wide, and <u>30</u> deep or <u> </u>	REGION <u>4</u>	COUNTY <u>71</u>	ID-NUMBER <u> </u>	DATE <u>9-20-83</u>
	STAFF <u>029</u>	INSTALLATION: ☒ 1. New Installation ☐ 2. Repair to Existing System		
	Type of System: ☒ 1. Standard ☐ 3. Chapter 301 ☐ 5. Other ☐ 2. Alternating ☐ 4. Chapter 212			
	For: ☒ 1. Residential; No. B/R <u>3</u> ☐ 2. Commercial/Industrial; Gal/Day <u> </u>			
Evaluation based Upon: ☐ 1. Soil Typing by Soil Scientist ☐ 2. Soil Percolation Tests ☒ 3. Other Permeability Rate <u>11.5 in/hr 45</u>				

The recipient of this permit agrees to construct or have constructed the system in accordance with the rules and regulations under the authority of TCA 53-2054. The recipient must notify the local health authority when the system is ready for inspection. If any part of system is covered before being inspected and approved, it shall be uncovered by the recipient of the permit at the direction of the local health authority.

 (Signature of Recipient-Owner, Developer, Contractor, Etc.) Date _____
 Issued at _____, Tennessee in the County of Putnam
 By _____ Date _____
 (Local Health Authority)

JD **RD**
 08/31/26 08/31/26

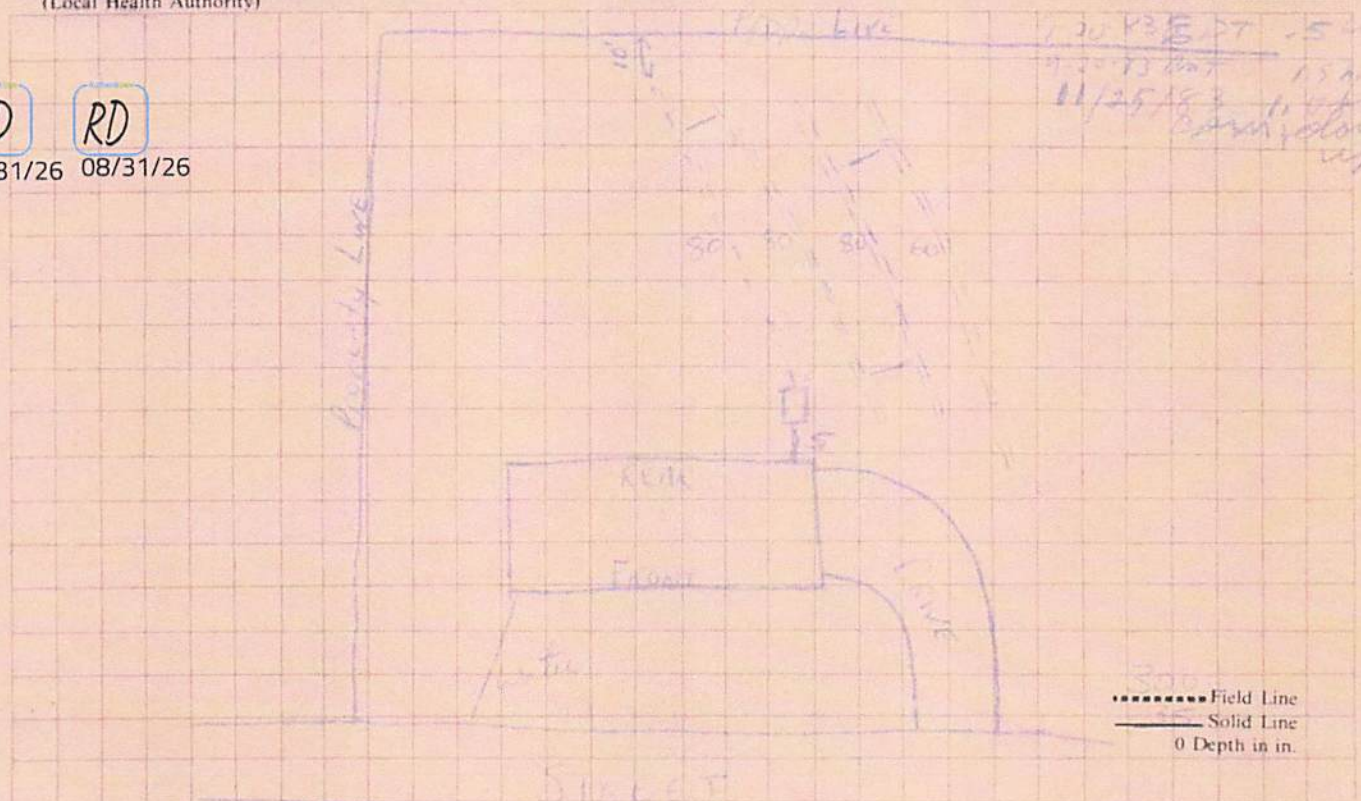

Inspected By James T. ...
 Local Health Authority
 Date 11-28-83

Construction Approval: ☐ 1. Yes ☐ 2. No
 No. of Visits: 1
 Time

--	--	--
