



PNR # 8453

20# 981349

CERTIFICATE OF COMPLETION OF SUBSURFACE SEWAGE DISPOSAL SYSTEM

Issued to: Garnentz Kris / Lisa
Location: 5188 Waddell Hollow Rd
Franklin TN 37064

Owner, Developer, Contractor, Installer, Etc.

GIS# 050--00518

7.07
1.1 ac

Type of system

- ☒ 1. Conventional
☐ 2. Low Pressure Pipe
☐ 3. Mound
☐ 4. Lagoon
☐ 5. Large Diameter Gravelless Pipe
(a) Sand backfill required Yes () No ()
☐ 6. Other

1250

Septic Tank

(type)

(volume)

Estimated Absorption Rate

(minutes per inch)


☒ New Installation

() Repair


() Other

Installed by:

Steve Pike

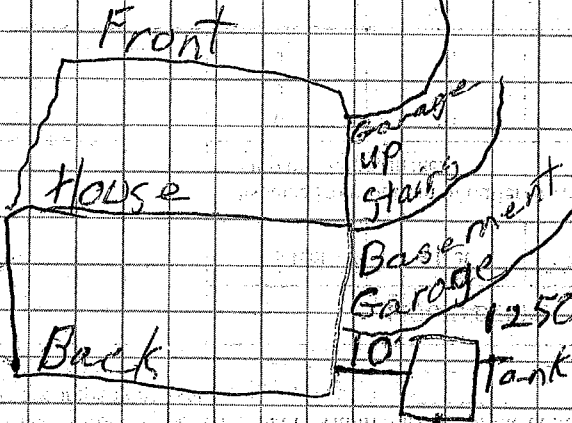

240' Curtain Drain

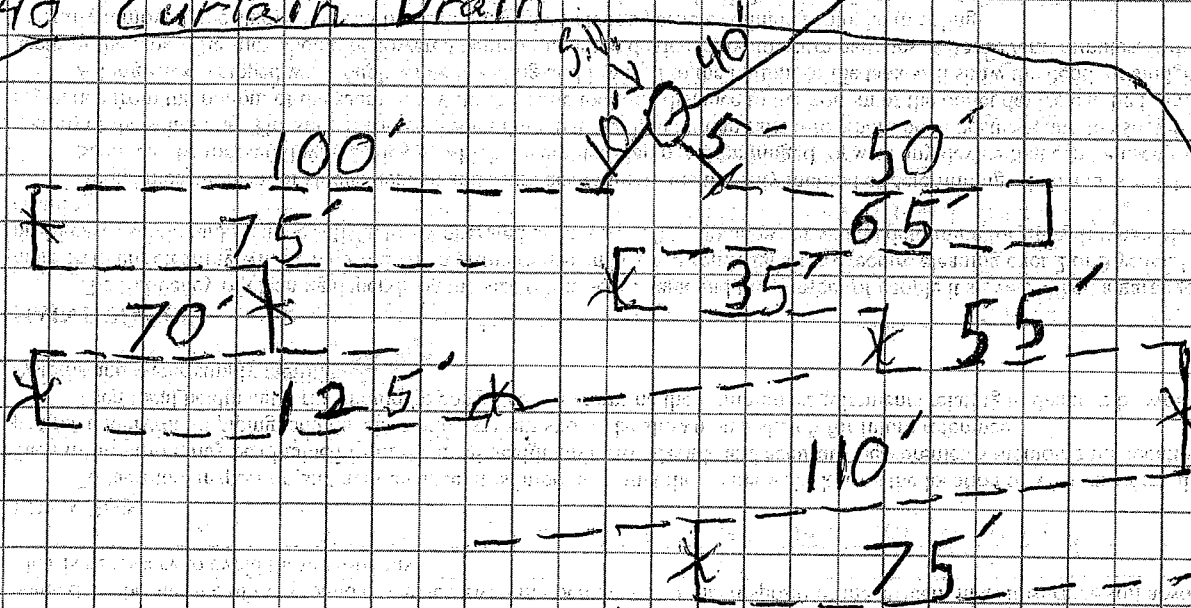

Construction Approved By:

Kris Pickett
(Name and Title)

4-23-99

(date)

pd 425.00 CKFF 1767 rec# 700

TENNESSEE DEPARTMENT OF ENVIRONMENT AND CONSERVATION
DIVISION OF GROUND WATER PROTECTION

PERMIT FOR CONSTRUCTION OF SUBSURFACE SEWAGE DISPOSAL SYSTEM

15281

Sept 11, 1998
Issued to: Gernentz, Kris, Lisa
Owner, Developer, Contractor, Installer, Etc.
Location: 5188 Waddell Hollow Rd
Franklin Tn
Installation:
() 1. New Installation
() 2. Repair to Existing System
Establishment:
() 1. Residential: # Bedrooms 4 bdr 90 gal tub.
() 2. Other: _____
(specify)
Gal/Day _____

Evaluation Based Upon:
() 1. Soil typing by Soil Scientist
() a. General
() b. High Intensity
() c. Extra High Intensity
(x) 2. Soil Percolation Test
(x) 3. Environmental Specialist
Estimated Absorption Rate: 75 MPI

Type of System:
(x) 1. Conventional
() 2. Low Pressure Pipe
() 3. Mound
() 4. Lagoon
() 5. Large Diameter Gravelless Pipe
a. Sand backfill required

ALL SEPTIC SYSTEMS MUST BE
INSTALLED BY AN INSTALLER
LICENSED IN THIS COUNTY.

NO BATHING FIXTURES TO EXCEED STANDARD
CIP NOT TO EXCEED 90 GALLONS, INCLUDING
OVERSIZED BATHTUBS, SPA-TUBS, HOT-TUBS,
WHIRLPOOLS OR SAUNAS, ETC., SHALL BE
ALLOWED UNLESS SPECIFICALLY APPROVED BY
THE WILLIAMSON COUNTY ENVIRONMENTAL OFFICE.

Also required:

- () 1. Soil Improvement Practice (SIP)
(x) 2. Flow Diversion Valve
() 3. Sewage Pump
(x) 4. Other: Interceptor / Curtain Drain

This system shall consist of a two compartment septic tank holding 1200
gallons, with 760 linear feet in 8-12 trenches, 36 inches
wide and 24 inches deep. (Depth of gravel: 12 inches)

All installers of subsurface sewage disposal systems must hold a valid annual license from the Tennessee Department of Environment and Conservation.

The recipient of this permit agrees to construct or have constructed the above described system in accordance with T.C.A. 68-221-401 et. seq. and The Regulations To Govern Subsurface Sewage Disposal Systems. If any part of the system is covered before being inspected and approved, it shall be uncovered by the recipient of the permit at the direction of personnel of the Department of Environment and Conservation. Any cutting, filling or alterations of the soil conditions on the aforementioned property after this day may render this approval null and void.

Don Babbins
(Signature of Recipient)

Date 10-5-98

Issued at Franklin

Tennessee, in Williamson

By E. J. W.C.S.O.
(Name and Title)

Date 9-23-98
(Date of Issue)

This permit is valid for 3 years from date of issue.

Notes

FIELD LINES, OF THE PRIMARY SEPTIC SYSTEM INSTALLATION, TO BE LOCATED WITHIN 1/2
OF THE AREA OF THE ACTUAL PERCOLATION TEST CONDUCTED
BY B.C. Tomlin ON 10-2-99. THE REMAINDER OF THE PERCOLATION TEST AREA IS
TO BE LEFT UNDISTURBED FOR USE AS THE SECONDARY SEPTIC FIELD AREA.

- A PUMP AND PUMP TANK (1200 GALLONS) MAY BE REQUIRED IF A GRAVITY FLOW (i.e.
CONSISTANT FALL MUST BE MAINTAINED THROUGHOUT THE ENTIRE LENGTH OF THE TIGHTLINE
FROM THE TANK TO THE SEPTIC FIELD NO SAGS) SYSTEM CANNOT BE INSTALLED FROM THE
EXISTING HOUSE-SITE TO THE APPROVED SEPTIC FIELD AREA

- ALTERNATING VALVE REQUIRED TO EQUALLY DIVIDE FIELD LINE FOOTAGE
CURTAIN DRAIN REQUIRED, THE DRAIN IS TO BE 36 INCHES DEEP AND
TAKEN TO A POSITIVE OUTLET.

- WATER LINE TO BE KEPT 10 FEET AWAY FROM THE PERCOLATION TEST AREA
- WELL TO BE KEPT A MINIMUM OF 50' AWAY FROM THE ACTUAL PERCOLATION TEST AREA.

APPROVED FOR ONE 4 BEDROOM SINGLE FAMILY DWELLING.
APPROVED FOR ONE 90 GALLON OVERSIZED BATHING FIXTURE.

NOTE: NO PART OF THE PERCOLATION TEST/SEPTIC FIELD AREA IS TO BE DISTURBED BY
COMPACTION, CUTTING, OR FILLING NOR IS ANY PART OF THE AREA TO BE ENCROACHED UPON
BY ANY PART OF A HOUSE, DRIVEWAYS, OR ANY UNDERGROUND UTILITIES

SPECIAL NOTE: ANY CUTTING GREATER THAN 18" FOR THE PURPOSE OF HOUSE CONSTRUCTION
MUST MAINTAIN 25' AWAY FROM THE ACTUAL PERCOLATION TEST AREA.

INSTALLER MUST CONTACT W.C.E.D. OFFICE PRIOR TO SEPTIC SYSTEM INSTALLATION FOR
LOCATION AND LAYOUT OF SYSTEM. INSTALLER TO CALL THIS DEPARTMENT FOR APPOINTMENT

NO utilities or their easements, above or below ground, shall be allowed to disturb or alter the natural state of
the soil areas reserved for sewage disposal, shall result in revocation of this permit.
Approach within 10 feet of the boundaries of the soil areas reserved for sewage disposal.
