

ENTERED

B

APPLICATION AND PERMIT FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM



LARIMER COUNTY
DEPARTMENT OF HEALTH & ENVIRONMENT
1525 BLUE SPRUCE DRIVE
FORT COLLINS, COLORADO 80524

- 1. 1/4 S 24 T 07 R 71 Parcel # 17240-00-052 (970) 498-6775 F.C.
- 2. Subdivision (970) 577-2050 E.P.
- 3. Lot 4 Block Filing Tract (970) 498-6772 FAX
- 4. New System X Repair Remodel Vault/Privy
- 5. Business Name
- 6. Addr/Loc 405 MOONDANCE WAY BELLVUE CO 80512
- 7. Owner HORNER, DONALD & JANICE Phone
- 8. Address 2493 GLENDALE CT LOVELAND CO 80538
- 9. Agent HORNER, DONALD Phone (970) 481-3599
- 10. Address 2493 GLENDALE CT LOVELAND CO 80538
- 11. Contractor HORNER, DONALD Phone
- 12. Address 2493 GLENDALE CT, LOV
- 13. Engineer Signature _____ Date 4
- 14. Build type SF Bsmt Bath Walk Out Capacity 7BDRMS Lot Size 35ACRES
- 15. Well Y Water Dist. Sanit. Dist.
- 16. Plot Plan X Eng. Report X Engineer's Design LANDMARK
- 17. Owner/Agent Signature *Donald Horner* Date 01/01/2003

Fee \$450⁰⁰ Receipt # *gd FC* BP # *03-80006* Cross Ref # *11415*

Permission is hereby granted to the owner or his agent to perform the work indicated below in accordance with the Larimer County Individual Sewage Disposal Regulations and is conditional upon the final installation approval of the Larimer County Department of Health and Environment. This permit is to remain in full force for the duration of the Larimer County Building Permit, or 120 days after its issuance, where applicable, providing it is not revoked for noncompliance. The issuance of this permit does not constitute assumption by the Department or its employees of liability for the failure or inadequacy of the sewage disposal system.

- 18. Depth to Water Table *> 20 ft* Perc Rate *59* Depth to bedrock *6 dig.* Slope _____
- 19. Type and Design of System *1250 gallon tank ~ 67 chambers installed in on-site fill area, at least 2.5 ft. from swale to the south and 100 ft. from proposed well. line downhill side wall perimeter of field down to native soil grade.*
- 20. Maintenance Schedule *Pump tank every 3-4 yrs.*
- 21. Please notify the department 48 hours in advance of backfilling to obtain final inspection for issuance of "Occupancy Certificate".

<u>Approval Signature</u>	<u>Date</u>	<u>Approval Signature</u>	<u>Date</u>
22. Preliminary: <i>Dmu</i>	<i>1/24/03</i>	24. Construction Inspection	
23. Site Inspection: <i>McCluskey</i>	<i>1/10/03</i>	25. Final inspection <i>McCluskey</i>	<i>2/18/04</i>
		26. Occupancy Permit Ok'd <i>TS</i>	<i>2/24/04</i>

Septic Tank: Gallonage size: 1250 Manufacturer: CPC

Absorption Area

- Gravel bed or trench square footage area _____
- Infiltrator or bio-diffuser units number 67 Hancor units
- SB2 Lineal footage _____

Evapotranspiration System (total or partial)

- Gravel bed square footage area: _____
- Infiltrator or bio diffuser unit number: _____


Vault or Privy Vault - Gallonage size: _____

Other: _____

Address: _____

DESIGN CODE 7

DIAGRAM

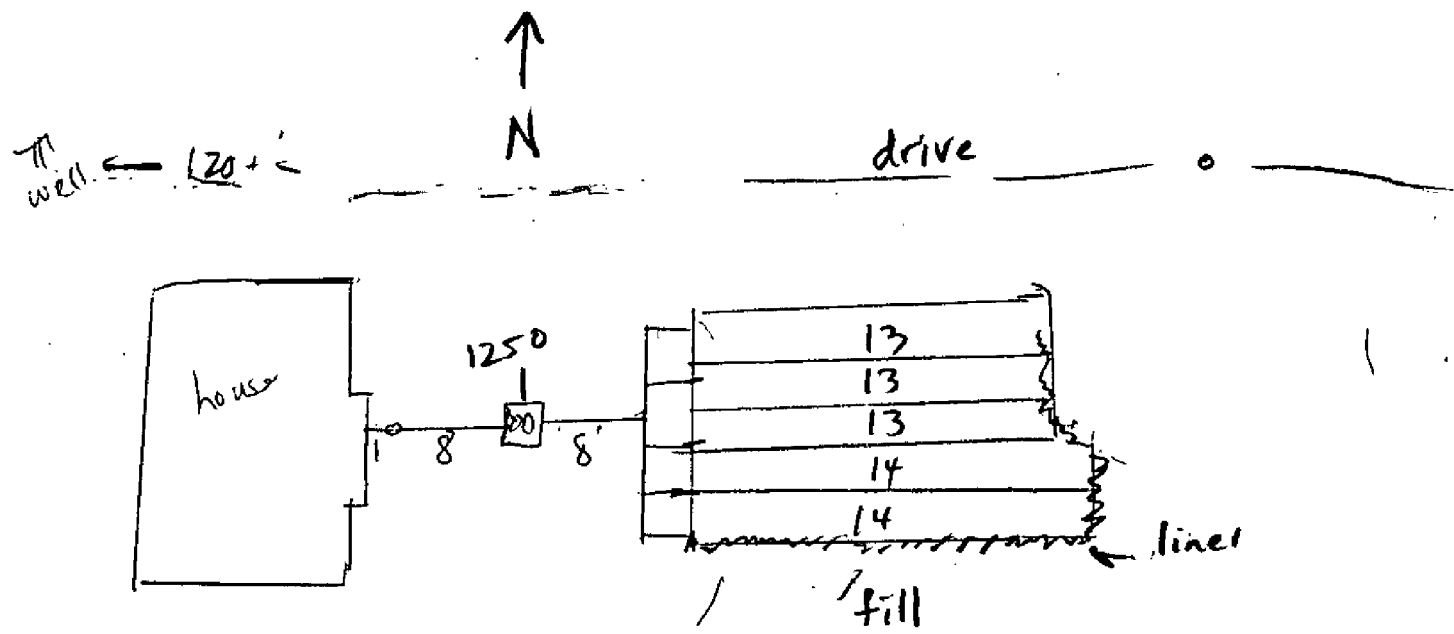

67 Hancor envirochambers
(standard)
